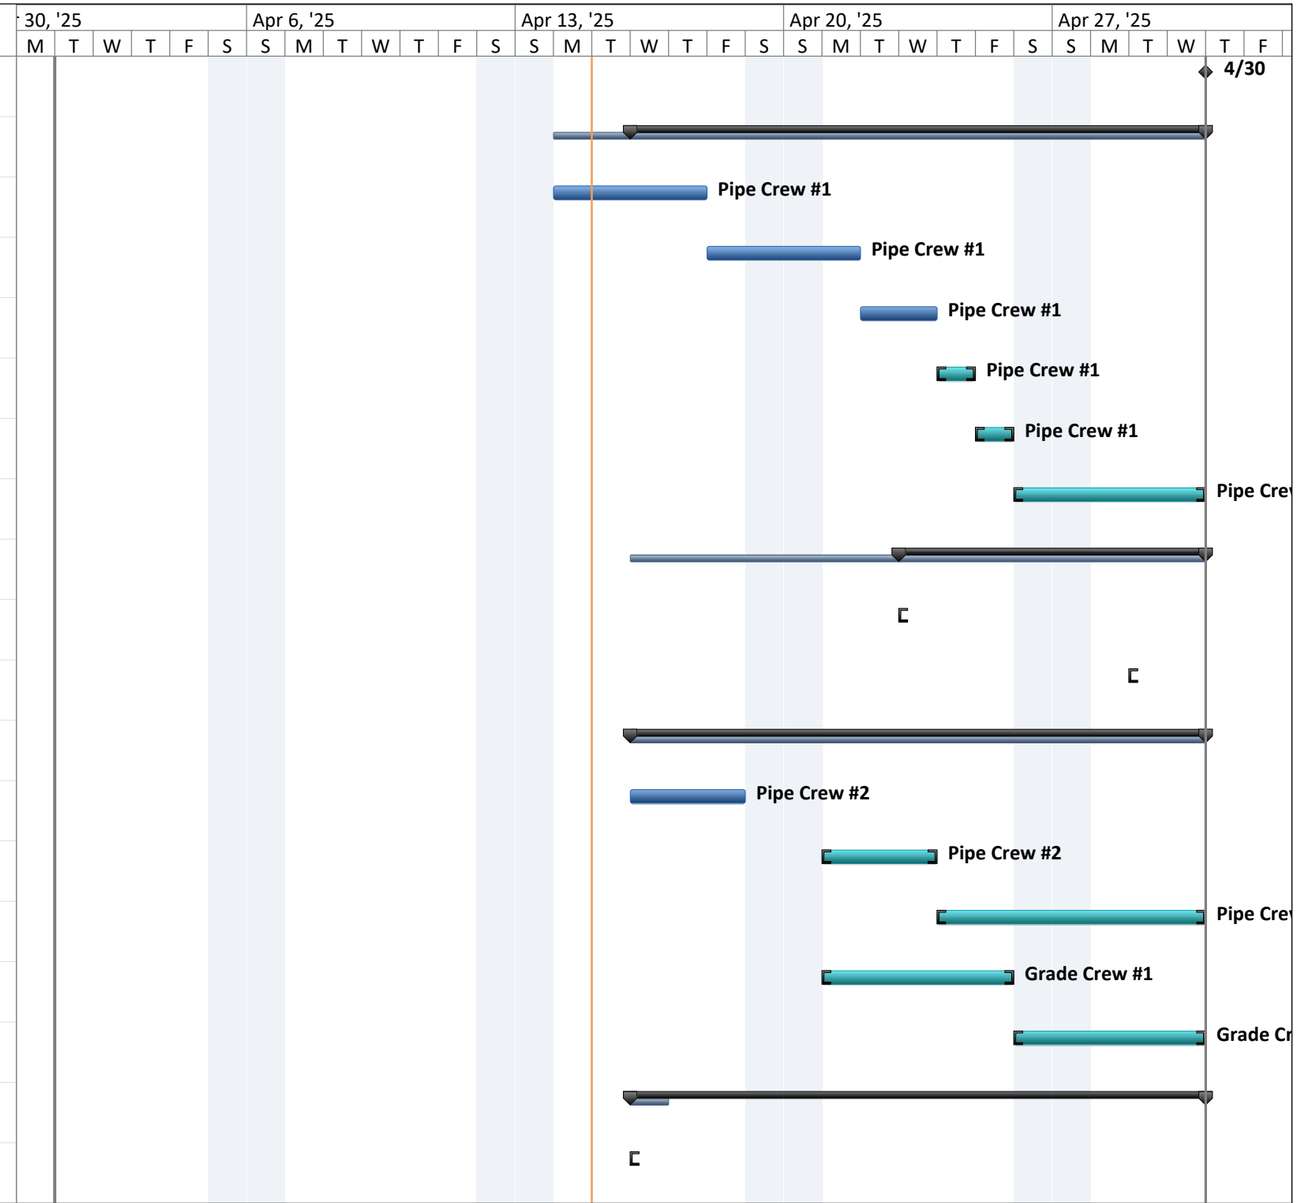ID	Task Name	Duration	Start	Finish	Crew/Subcontractor
1	NH-CR 0014(185)229 (PCN X05W)	0 days	Wed 4/30/25	Wed 4/30/25	
2	**Phase 1A Sta 9+50 to Sta 10+00**	**11 days**	**Wed 4/16/25**	**Wed 4/30/25**	
3	Sanitary Sewer Bypass	4 days	Mon 4/14/25	Thu 4/17/25	Pipe Crew #1
4	Set Manhole #926, tie in and install new pipe	2 days	Fri 4/18/25	Mon 4/21/25	Pipe Crew #1
5	Pavement Removals	2 days	Tue 4/22/25	Wed 4/23/25	Pipe Crew #1
6	Water Main Tie in at station 210+72	1 day	Thu 4/24/25	Thu 4/24/25	Pipe Crew #1
7	Install 14" H20 to Temp Cap	1 day	Fri 4/25/25	Fri 4/25/25	Pipe Crew #1
8	Sub Base Prep	4 days	Sat 4/26/25	Wed 4/30/25	Pipe Crew #1
9	**Phase 1A Subcontractors**	**6 days**	**Wed 4/23/25**	**Wed 4/30/25**	
10	Muth		Wed 4/23/25		
11	Sharpe		Tue 4/29/25		
12	**Phase 2A**	**11 days**	**Wed 4/16/25**	**Wed 4/30/25**	
13	14" PVC Watermain to Capitol	3 days	Wed 4/16/25	Fri 4/18/25	Pipe Crew #2
14	Water Service Install X3	3 days	Mon 4/21/25	Wed 4/23/25	Pipe Crew #2
15	RCP Install	5 days	Thu 4/24/25	Wed 4/30/25	Pipe Crew #2
16	Sidewalk/Curb Removals	5 days	Mon 4/21/25	Fri 4/25/25	Grade Crew #1
17	Sub Base Prep	4 days	Sat 4/26/25	Wed 4/30/25	Grade Crew #1
18	**Phase 2A Subcontractors**	**11 days**	**Wed 4/16/25**	**Wed 4/30/25**	
19	TerraTech		Wed 4/16/25
